Plainview-Old Bethpage CSD 2014 Bond Referendum & Capital Projects Update



August 12, 2019

Construction Overview

- The District will complete about \$17 million in construction work between June 2019 and December 2019.
- ➤Of the \$49.7 million Bond passed by voters in 2014, the District has committed \$44.4 million or almost 90% of total funding. Most of the work still to be completed is at Stratford Road.
- ➤ Work has been taking place in all seven schools.
- Some work will continue into the school year.

POBJFK HS Projects


| Project | Comments | Status as of 9/4 |
|--|--------------|----------------------------|
| Interior/Exterior Masonry | Begin August | Complete August |
| Window Replacement | Begin August | Complete Spring 2020 |
| Gym Curtain Installation | In progress | Complete September |
| Boiler Replacement | In progress | Complete late September |
| Main Office and Guidance Carpet Replacement | Complete | Completed July |
| Social Studies Office Renovation | In progress | Complete August |
| Library Carpet Replacement in main student areas | Complete | Completed July |

POBJFK HS Progress











POBJFK HS Progress







Part of Window Replacement project is trim painting from white to blue.

New Boiler installation in progress

POB Middle School Projects

| Project | Comments | Status as of 9/4 |
|--|--------------------------|------------------|
| Renovations Rooms 109 & 110 and zSpace | In progress | Complete August |
| Prep Room Abatements 2 nd Floor | Complete with new floors | Completed July |
| Renovation Rooms 204 and 206 | In progress | Complete August |



POB Middle School Progress





Making a new classroom in first floor tech for a total of three rooms.

POB Middle School Progress





zSpace classroom moved to a new space in the Library

Room 302 prep room flooring installation in progress

POB Middle School Progress



New classrooms converted from old faculty room space





FACS Room Renovation

New age-appropriate playground

Mattlin Middle School Projects

| Project | Comments | Status as of 9/4 |
|--|-------------|------------------|
| Interior/Exterior Masonry | In progress | Complete August |
| C & D House Wheelchair Lift Replacement | In progress | Complete August |
| Renovate Boys and Girls Locker Rooms | In progress | Complete August |



Mattlin Middle School Progress



Locker Room renovation

New chairlifts in C and D Houses

Exterior masonry retaining wall work

Judy Jacobs Parkway Projects

| Project | Comments | Status as of 9/4 |
|--|------------------|------------------|
| Roof & Skylight Replacement | Starts late July | Complete August |
| Interior/Exterior Masonry | Begins August | Complete August |
| Electrical Upgrades (PA Replacement and Hand Driers) | Begins August | Complete August |

Judy Jacobs Parkway Progress





New roofing and ventilation fans. Skylights to be replaced.

Old Bethpage Projects

| Project | Comments | Status as of 9/4 |
|---|-------------|-------------------------|
| Classroom Addition and Parking Expansion | In Progress | Complete Fall 2019 |
| Boiler Replacement | In progress | Complete late Sept 2019 |





Roof of addition during construction



New driveway and side of addition





Exterior wall of classroom addition with exterior brick being installed.

Interior of classroom addition in progress.



Work continues to get ready for the beginning of the school year



Getting boiler room ready for new boiler



New boiler

Pasadena Projects

| Project | Comments | Status as of 9/4 |
|----------------------------------|------------------------|-------------------------|
| Roof & Skylight Replacement | In progress (90% done) | Complete August |
| Boiler Replacement | In progress | Complete late September |
| Replace Music Room Floor | Complete | Completed July |
| Replace Principal's Office Floor | Complete | Completed July |



Pasadena Elementary Progress





New flooring installed in Music room

New roofing with in-house fans installed and sealed

Stratford Road Projects


| Project | Comments | Status as of 9/4 |
|---|-------------|-------------------------|
| Ceiling and Lighting Replacement | In progress | Complete August |
| Boiler Replacement | In progress | Complete late September |
| Electrical Upgrades (PA Replacement and Hand Driers) | In progress | Complete August |



Stratford Road Elementary Progress



Ceiling and lighting replacement project in progress

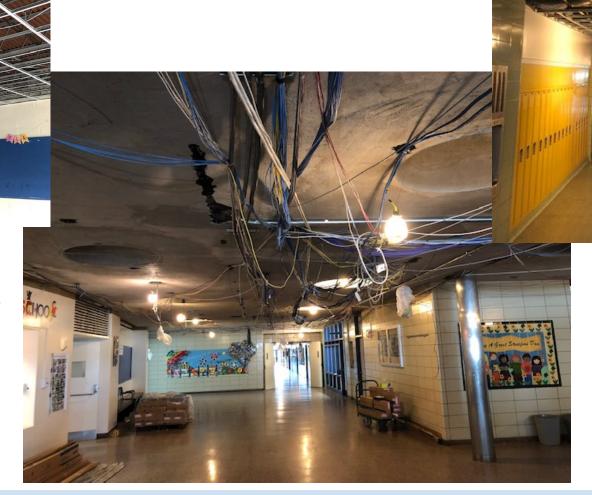

Stratford Road Elementary Progress









New boiler and high efficiency burners







A Smart Investment THANK YOU!
