Plainview - Old Bethpage Central School District

2014 Bond Referendum & Capital Improvement Projects Update

March 21, 2016



Plainview - Old Bethpage Central School District

Parkway Elementary School

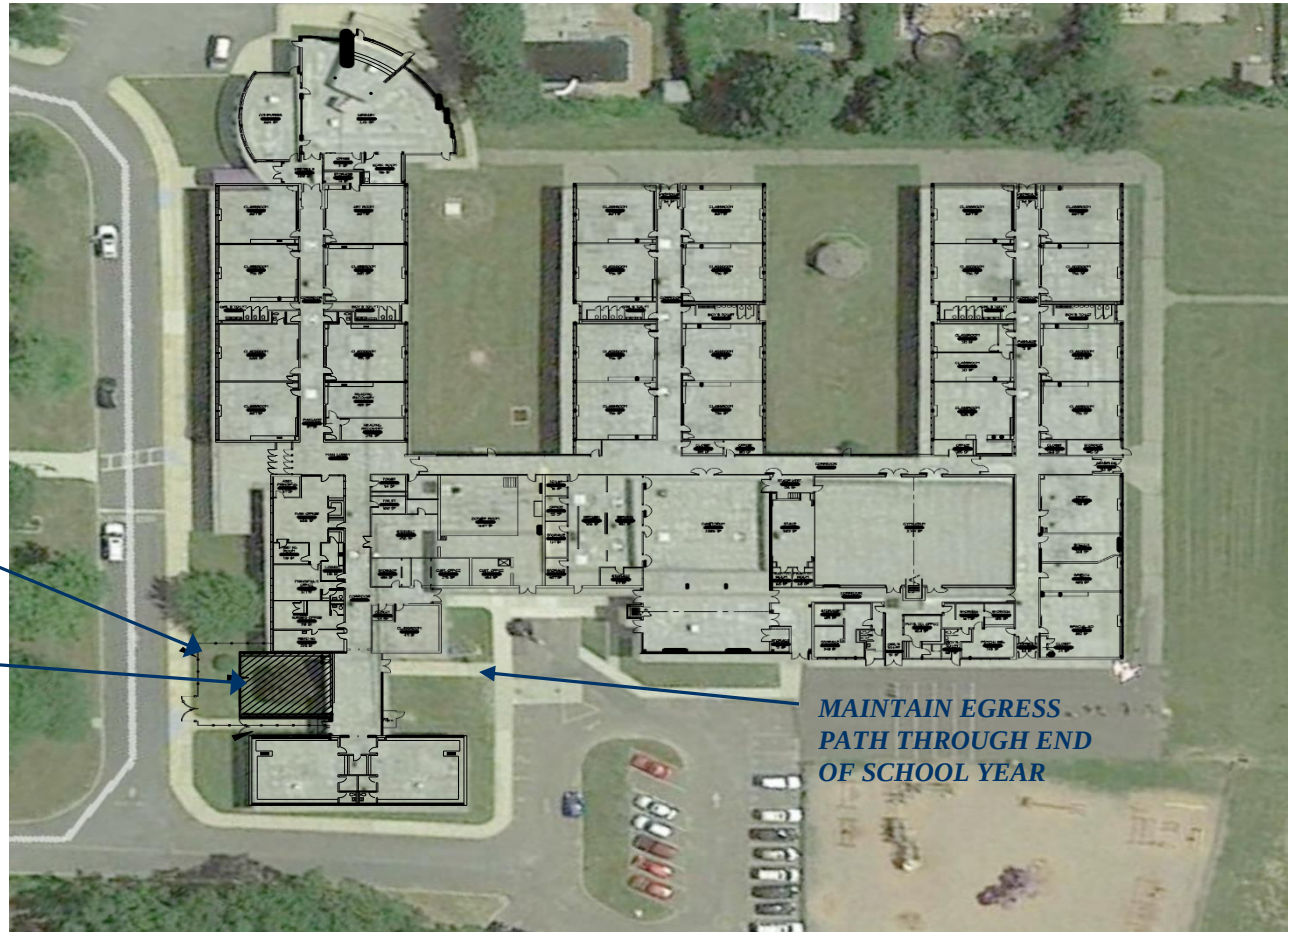

PLAINVIEW-OLD BETHPAGE CENTRAL SCHOOL DISTRICT

PARKWAY ELEMENTARY SCHOOL

BBS Architects Landscape Architects Engineers

NOT TO SCA

SK-5

3•16•16

Plainview - Old Bethpage Central School District

Pasadena Elementary School

PLAINVIEW-OLD BETHPAGE CENTRAL SCHOOL DISTRICT

PASADENA ELEMENTARY SCHOOL

BBS
Architects
Landscape Architects
Engineers

NOT TO SCALE

SK-6

3•16•16

Plainview - Old Bethpage Central School District

Anticipated Classroom Construction Timeline

Construction to start on:

April 8th 2017 – April break

- Contractor or contractors are responsible to install temporary fencing.
- Install temporary partitions, maintaining egress which allows for construction to continue during school days.
- Demo interior spaces as needed, understanding spaces outside of the demo areas will be occupied by **April 17th**.

April 16th 2017 –

- Egress paths / temporary partitions must be completed, classes to resume **April 17th**.

June 26th last day of classes, contractor will have full access of construction areas.

August 25th Substantial completion (occupancy). All construction materials and tools removed from site.

August 31 Punch-list completed. All temporary fencing and partitions removed.

September 30th final closeout

Plainview - Old Bethpage Central School District

Anticipated Classroom Construction Timeline

April 2017

Construction preparation to begin simultaneously at Parkway and Pasadena Elementary Schools during Spring Recess

August 2017

Substantial completion (buildings ready for occupancy in September – construction materials removed)

September 2017

Completed!!!

Plainview - Old Bethpage Central School District

Timeline – Pending Projects

April 2016 – June 2017

District-wide interior doors/hardware replacement

(Awaiting Bid Opening)

July 2016- June 2017

Window/door replacements at POBMS, Parkway, Pasadena and Jamaica Avenue

June 2016- September 2016

Remaining Phase I projects- Stratford Road floors, Old Bethpage crawlspace

Plainview - Old Bethpage Central School District

Design Phase

- **ADA Accessibility Upgrades** - POB JFK High School, POB Middle School, Mattlin Middle School, Parkway School, Pasadena School, Stratford Road School, and Jamaica Avenue School
- **Auditoriums** – POB JFK High School, POB Middle School, Mattlin Middle School, Stratford Road School
- **Security Upgrades** – District-wide
- **Technology Upgrades** – District-wide

Plainview - Old Bethpage Central School District

Other Capital Projects

Upcoming Capital Projects

- Boiler Replacements at Mattlin MS (Work begins April 2016)
- JFK HS Roof Replacement (Summer 2016)
- POB JFK HS Parking Lot Reconstruction (Summer 2016)
- District-wide Door Replacements (incorporated into Bond phasing)
- JFK HS Window Replacements (Summer 2017)

POB Schools:
A Smart Investment

Thank You
